KK GIRDER PROJECT

Girders Daily Status Report

Date: Wed Nov 11 2026 09:58:06

Daily Progress Summary

Sr	Items	Prev	Oct 28	Oct 29	Oct 30	Oct 31	Nov 01	Nov 02	Nov 03	Nov 04	Nov 05	Nov 06	Nov 07	Nov 08	Nov 09	Nov 10	Nov 11	Total
1	Girders Concreted	314	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	314
2	Girders Stressed	298	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	298
3	Girders Grouted	297	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	297
4	Girders Launched	279	0	0	0	0	0	0	0	0	0	0	0	0	0	10	0	289
5	Diaphragms Concreted	30	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Production Breakdown

Girders Concrete (In / Out)

Month	Factory	Yard	Total
Old			30
Jan	0	0	0
Feb	0	7	7
Mar	0	20	20
Apr	5	36	41
May	10	16	26
Jun	15	5	20
Jul	16	23	39
Aug	41	32	73
Sep	31	18	50
Oct	3	5	8
Nov	0	0	0
Total	121	162	314

Girders Casted By Contractor

Contractor Name	Girders Concreted
Athar Awan	86
Sultan Shah	43
Aftab Ahmed	19
Akbar Khan	106
Company	16
Wada Mistari	30
Abid Ali	14
Total	314

Diaphragms Concreted By
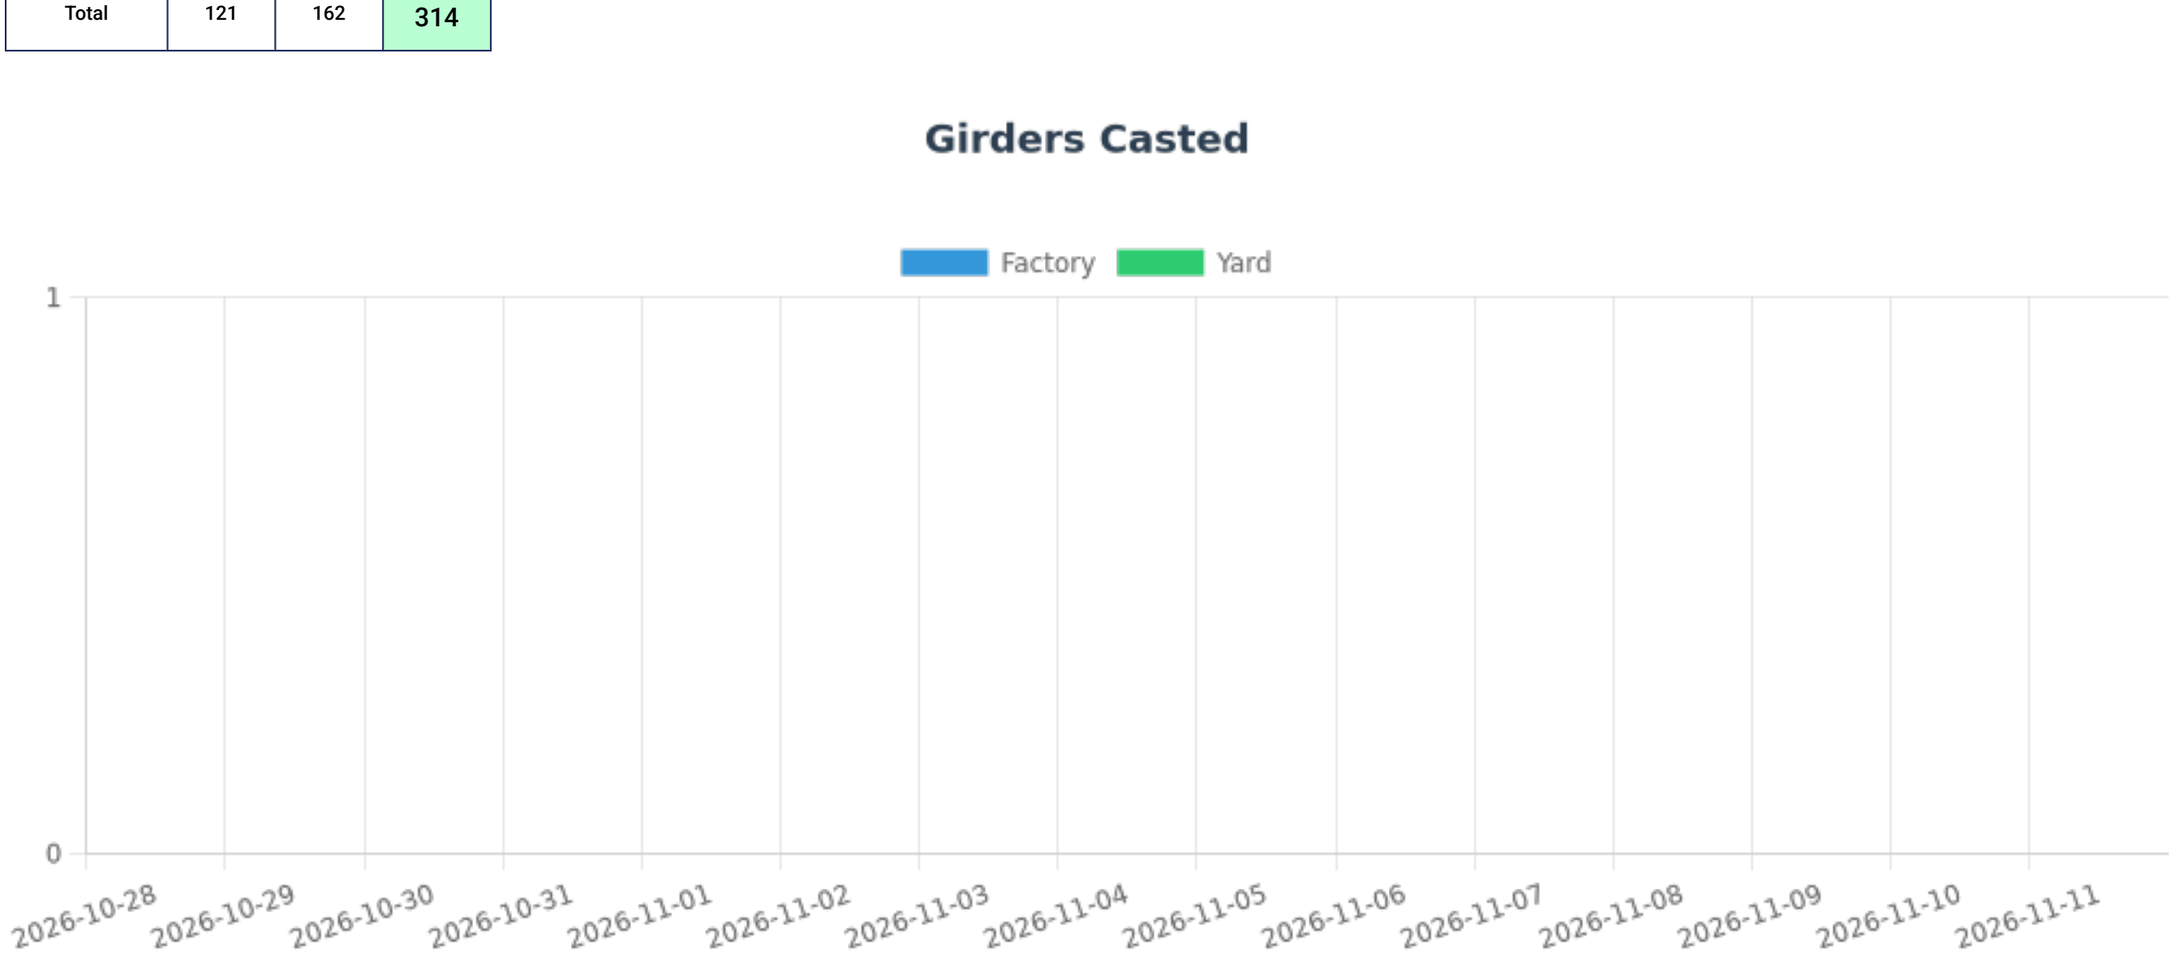
Contractor Name	Diaphragms Concreted
Athar Awan	15
M Atif	15
Total	30
